UNIVERSITY OF WOLVERHAMPTON

Project Management 6.3

Project Governance Roles

UNIVERSITY OF WOLVERHAMPTON

Learning Outcomes

- By the end of this week, you will be able to:
  - Be aware of roles and responsibilities
  - State the roles required for a project
  - Discuss change control
  - Give relevant examples of governance roles.


UNIVERSITY OF WOLVERHAMPTON

Governance

- Governance is the project manager's friend
  - It gives us clear boundaries to our authority
  - It gives us a clear route for questions and requests
  - It provides a process for ensuring that what we are delivering is what the organisations wants / expects
  - It makes clear; responsibilities and accountabilities as well as who needs to be consulted or informed

Responsibilities (using PRINCE2 terminology)

- Project Board
  - During Start up and Initiation
  - During the Project
  - At the end of a Project
- Executive
  - Not a Democracy
  - Ultimate Responsibility
    - Supported by:
      - Senior User
      - Senior Supplier

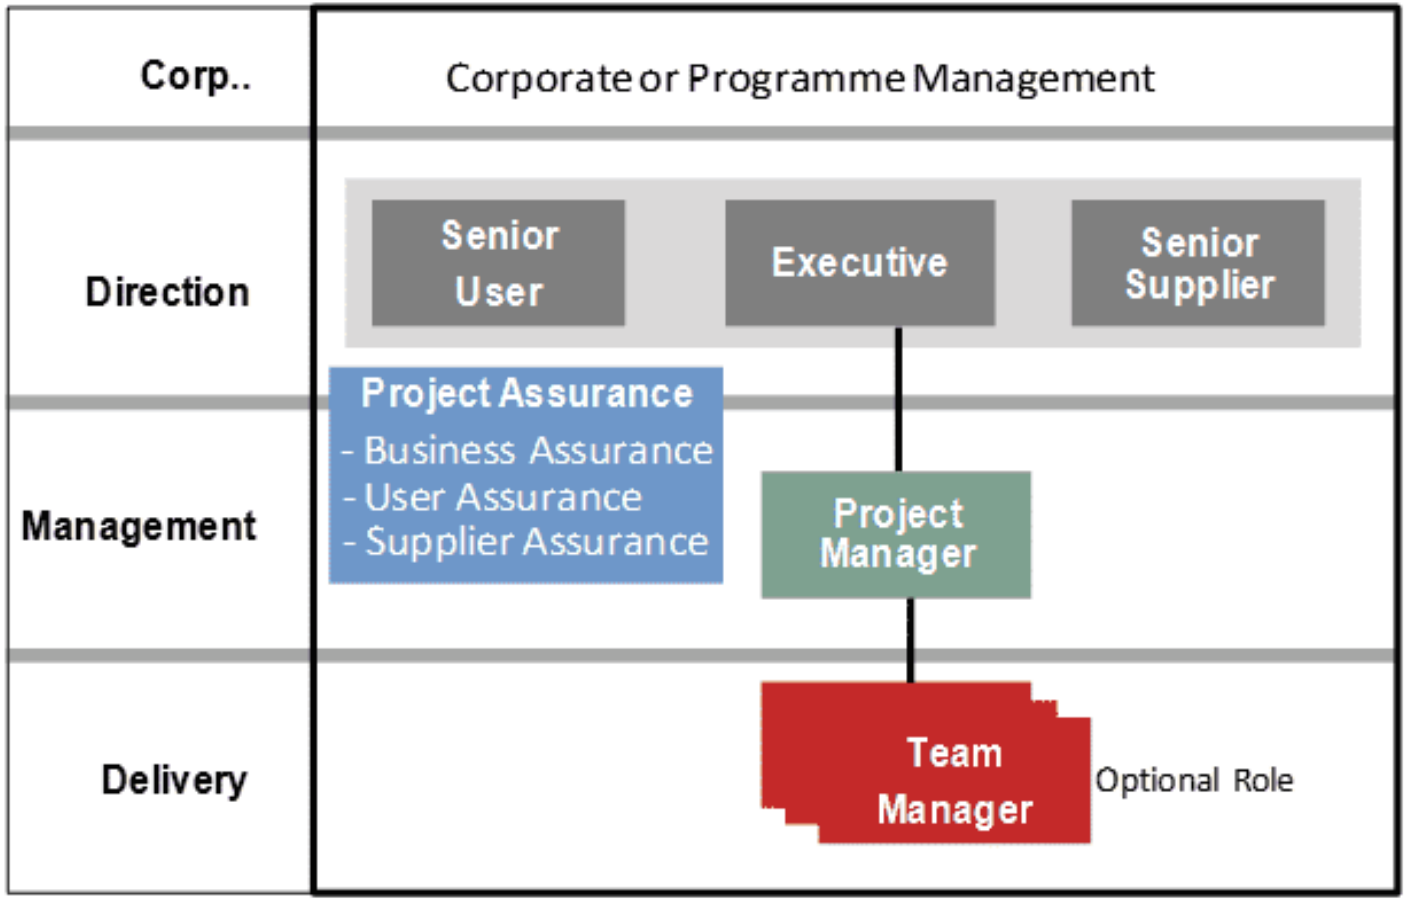

UNIVERSITY OF WOLVERHAMPTON

Roles & Responsibilities – Senior User

- Senior User
  - Responsible for specifying users needs
  - Liaison with the project management team
  - Ensures the product meets:
    - Quality
    - Functionality
    - Ease of use

Roles & Responsibilities – Senior Supplier

- Senior Supplier
- Represents the Interests of:
  - Those designing, developing, facilitating, procuring and implementing the projects products
- Accountable for the quality of products delivered
- Responsible for the technical integrity of the project

Roles & Responsibilities – Project Manager

- Project Manager
  - Prepare management products
  - Prepare reports
  - Maintain Records
- Liaise with corporate or programme management
- Liaise with any external suppliers
- Lead and motivate the project team
- Ensure that behavioural expectations of team members are established
- Manage the information flows between the directing and delivering levels of the project

Roles & Responsibilities – Team Manager

- Team Manager
  - Prepares Team Plans
  - Produces Checkpoint reports
  - Plan, monitor and manage the team's work
  - Takes responsibility for the progress of the team
  - Advises on Risks and issues
  - Passes back completed work packages
  - Liaise with any Project Assurance and Project Support
  - Ensure quality activities are planned and performed correctly

UNIVERSITY OF WOLVERHAMPTON

Roles & Responsibilities- Project Assurance

- Asks questions to ensure:
  - Liaison is maintained between the business, user and supplier
  - Risks are controlled
  - The right people are involved in writing Product Descriptions
  - People are involved in quality inspection at the correct points
  - Staff are properly trained in the quality methods
  - Quality control follow-up actions are dealt with correctly
  - An acceptable solution is being developed
  - The scope of the project is not changing unnoticed
  - Internal and external communications are working
  - Applicable standards are being used
  - The needs of specialist interests are being observed

Roles & Responsibilities – Change Authority

Change Authority

- The Change Authority should:
  - Be capable of adequately representing the business, user and supplier stakeholder interests
  - Have sufficient credibility to ensure that advice and guidance are followed
  - Have sufficient specialist knowledge of the business, user or supplier stakeholder areas.

UNIVERSITY OF WOLVERHAMPTON

Roles and Responsibilities

- Each role should have a job description which will help;
  - Recruit a suitable post holder
  - Outline their responsibilities
  - List key skills or training needed for the role to support recruitment, development and coaching
  - Make clear reporting lines and other key information about the role
- The level of qualifications and the amount of experience required will usually be a reflection of the size, value or importance of the project

Job Description

- There is no one right way to lay out a job description as different organisations will have their own conventions and preferences
  - Example job description:



PM

UNIVERSITY OF WOLVERHAMPTON

Governance

- The importance of governance cannot be overstated
- It is there to establish project parameters, NOT to tell participants how to carry out project goals
- Each Role will have a job description, including products and areas that they are responsible for
- There are tools to assist us with this, like RACI diagrams

UNIVERSITY OF WOLVERHAMPTON

Look Forward

- L6.4 Project Lifecycles
